

CLEPSO

PRODUCT & ENGINEERING

Keep every matter moving.

A full US practice-management suite.
Every practice area. Staff and client applications.
One connected model for work, information, and money.

DOCUMENT	CONFIRMED DIRECTION
Version / date	1.1 / October 1, 2026
Initial firm sizes	Solo practitioners through approximately 50 lawyers
Geography	Nationwide US core support; sourced jurisdiction-specific automation
Practice coverage	Universal core, configurable profiles, dedicated specialty modules
Delivery	23 modules (M00-M22); core launch before AI receptionist
Status	Implementation specification and roadmap; not evidence of completed features

Final-module decision

The AI receptionist is evaluated and implemented last. Application-owned, n8n-assisted, managed-API, and hybrid approaches remain open.

IMPLEMENTATION BLUEPRINT

Document map

Product direction, architecture, and implementation modules

Use module identifiers in engineering tickets and review discussions. Page references follow the fixed document sections; modules describe outcomes and dependencies rather than staffing or calendar promises.

PAGE	SECTION
1	Cover and confirmed direction
2-3	Document map and module index
4	Product scope and launch requirements
5	Operating-map findings and product implications
6	Competition and differentiation hypotheses
7	Current repository audit
8	Architecture and authorization flow
9	Domain contracts and nationwide model
10	Delivery waves and dependency map
11-33	M00-M22 module implementation chapters
34-35	Practice families and specialty delivery
36	Jurisdiction and automation coverage
37-38	Flagship end-to-end journeys
39-40	Acceptance, failure, and recovery testing
41	Core release and operations
42	External dependencies and deferred decisions
43-44	Sources and decision history

How to use this document

Implement shared foundations first, then complete each module through its acceptance gate. A demo screen is not a completed module; live records, permissions, recovery, and service outcomes must also work.

IMPLEMENTATION BLUEPRINT

Module index

The full feature set, divided into 23 implementation modules

MODULE	SUBSYSTEM	POSITION
M00	Engineering platform and delivery foundation	Core / supporting
M01	Identity, firm provisioning, and access	Core / supporting
M02	Contacts, parties, matters, and configurable profiles	Core / supporting
M03	Integration and synchronization framework	Core / supporting
M04	Documents, templates, storage, and signatures	Core / supporting
M05	Communications, inbox, and notifications	Core / supporting
M06	Tasks, calendars, deadlines, and obligations	Core / supporting
M07	Intake, conflicts, engagement, and onboarding	Core / supporting
M08	Editable templates and durable workflow engine	Core / supporting
M09	Time, expenses, and staff capture	Core / supporting
M10	Billing, invoicing, and revenue management	Core / supporting
M11	Payments, trust accounting, and reconciliation	Core / supporting
M12	AI platform, retrieval, and proposal governance	Core / supporting
M13	Seven flagship connected automations	Core / supporting
M14	Document intelligence and external legal research	Core / supporting
M15	Production staff web and native experience	Core / supporting
M16	Client portal and native client applications	Core / supporting
M17	Reports, workload, and firm management	Core / supporting
M18	Nationwide profiles and specialty modules	Core / supporting
M19	Migration, export, closure, and retention	Core / supporting
M20	Subscriptions, AI usage, and spending controls	Core / supporting
M21	Nationwide validation and core launch	Core release gate
M22	AI receptionist: evaluate, decide, then implement	Post-launch / last

Dependencies

M15 frontend work and M18 practice profiles develop alongside their supporting domains. M21 validates the complete core release. M22 is deliberately outside the core launch dependency chain.

IMPLEMENTATION BLUEPRINT

Nationwide, every practice area

The scope agreed for the product

Required product surfaces

- Staff web application and native iOS/Android staff applications.
- Client web portal and shared Clepso iOS/Android client applications, with firm branding inside the authenticated experience.
- Microsoft 365 and Google email/calendar connectivity; deeper Word/Outlook filing, context, and drafting support developed first.

Required operating capabilities

- Intake, conflicts, engagement, parties, matters, documents, signatures, communications, calendars, tasks, and closure.
- Capture, time, expenses, multiple fee models, billing, payments, retainers, trust records, reconciliation, and reporting.
- Editable practice templates, dependencies, assignments, reminders, approval gates, migration, export, and access controls.
- All seven flagship automations; source-linked drafting, document review, factual chronology, and specialist legal research.

Coverage and delivery

- Nationwide core support does not depend on California law or a small fixed practice-area list.
- All practice families operate through configurable shared models; specialized tools arrive through released specialty packs.
- Initial firm-size focus remains approximately 50 lawyers or fewer. No enterprise-at-launch assumption is added.
- Core launch precedes the AI receptionist. Its implementation approach will be selected in M22 after deeper evaluation.

What is already decided

Use controlled autonomy, published client information, editable operational templates, and included AI allowances with clear usage and caps. No fixed launch date, final pricing, or receptionist supplier has been decided.

IMPLEMENTATION BLUEPRINT

What the operating map means for the product

Translate the research into practical product requirements

OPERATING PATTERN	PRODUCT RESPONSE	PRIMARY MODULES
Information arrives across email, calls, documents, and portals.	Connect source channels; file information explicitly; preserve evidence and sync health.	M03-M05, M12-M13
Tasks depend on missing information, other people, and external responses.	Track prerequisites, ownership, requests, blockers, and completed follow-through.	M06, M08, M13
Delegated work still requires professional supervision.	Maintain bounded authority, approval gates, source history, and reversible operational actions.	M01, M08, M12
Clients want progress, next steps, responsiveness, and cost clarity.	Publish understandable updates; show requests, messages, signatures, invoices, and receipts.	M05, M10-M11, M16
Different fee models change the value of faster work.	Support actual hourly capture, flat-fee scope/cost visibility, and contingency progress/cost records.	M09-M11, M17
Migration and trust in financial records affect switching.	Reconcile imports and independent financial evidence; provide complete export.	M11, M19
Small teams need coverage; larger teams need handoffs and oversight.	Add backups, matter access, workload, responsible people, and preparation briefs.	M01, M06, M13, M17

Evidence boundaries

The supplied operating-map document is a broad research synthesis. It explicitly distinguishes vendor surveys, regional findings, dated datasets, and unmeasured questions. This blueprint preserves those distinctions instead of turning every statistic into a universal product claim.

Validation requirement

The value hypothesis is less coordination and correction effort, with more completed follow-through. Establish this through realistic workflows and pilots. The exported research contains placeholders for embedded figures; no missing charts have been reconstructed. [S01]

IMPLEMENTATION BLUEPRINT

The competitive bar

Existing capabilities establish the baseline; execution quality must be tested

COMPETITOR	RELEVANT DOCUMENTED / ADVERTISED CAPABILITIES	SOURCE
Clio	Matter catch-up, proactive action suggestions, communication drafts, scheduling and billing assistance.	S03
MyCase	Passive time capture and case questions spanning documents, messages, tasks, and financial records.	S04
Smokeball	Matter-aware drafting, cited answers, document discrepancy review, and Word/Outlook assistance.	S05
Filevine	Document deadline extraction, task/deadline chains, and records-related integrations.	S06
Litify	Proactive case analysis and multi-step agentic workflow execution.	S07
Actionstep	Operational workflows, time capture, business intelligence; reviewed page labeled orchestrated AI workflows coming soon.	S08
PracticePanther	Intake, messaging, task automation, billing, and client portal functions.	S09

Differentiation to prove

- One coherent review from source event to changed work, client update, and tracked execution.
- Useful blocker detection and preparation dependencies, not merely more notifications.
- Client requests that visibly connect upload, review, next step, and published progress.
- Production mobile follow-through with the same authoritative records as staff web.
- Financial and workflow outcomes users can inspect, correct, and reconcile.

Claims versus outcomes

These sources establish advertised or documented capability, not measured comparative quality. Do not claim incumbents lack a feature without verification. Test setup effort, review effort, reliability, and task completion against current firm processes.

IMPLEMENTATION BLUEPRINT

Repository baseline

What can be reused and what still needs production implementation

AREA	OBSERVED STATE	REQUIRED WORK
Staff web	Substantial interactive screens and local demo flows.	Replace in-memory domain data, fixture AI, simulated delivery, and aggregate placeholders.
Staff native	Expo preview, persisted timer, shared design primitives; large preview state machine.	Production routes, domain forms, data hooks, offline recovery, and platform parity.
API	NestJS health/auth modules and authentication guard.	Domain modules, authorization, transactions, commands, and OpenAPI contracts.
Worker	BullMQ heartbeat processor.	Durable processing, outbox dispatch, scan/extraction, reminders, integrations, and AI tasks.
Database	Tenancy/auth foundations and RLS migrations.	Business schemas, matter grants, audit records, workflows, documents, finances, and client publication.
Client products	Design reference; portal reserved.	Client identity, portal and native apps, published views, actions, and notifications.
Practice model	Six fixed frontend practice-area values and demo playbooks.	Configurable taxonomy, profiles, multi-jurisdiction matters, and versioned workflows.
Marketing	Landing application exists in the current working tree.	Keep claims aligned with actual launch coverage; unrelated edits remain untouched.

Reuse boundaries

Retain the Clepso design system, shared money/duration conventions, API write rule, schema/migration history, and existing frontend seams. Treat preview copy as a product example rather than a validated legal rule or connected service. [S02]


Implementation warning from the audit

Demo trust balances are not independent bank evidence; prose-parsed deadline chains are not a rules engine; a success toast is not a delivery confirmation. Production modules must replace those assumptions explicitly.

IMPLEMENTATION BLUEPRINT

One authoritative operating model

Application-owned state, bounded commands, recoverable processing

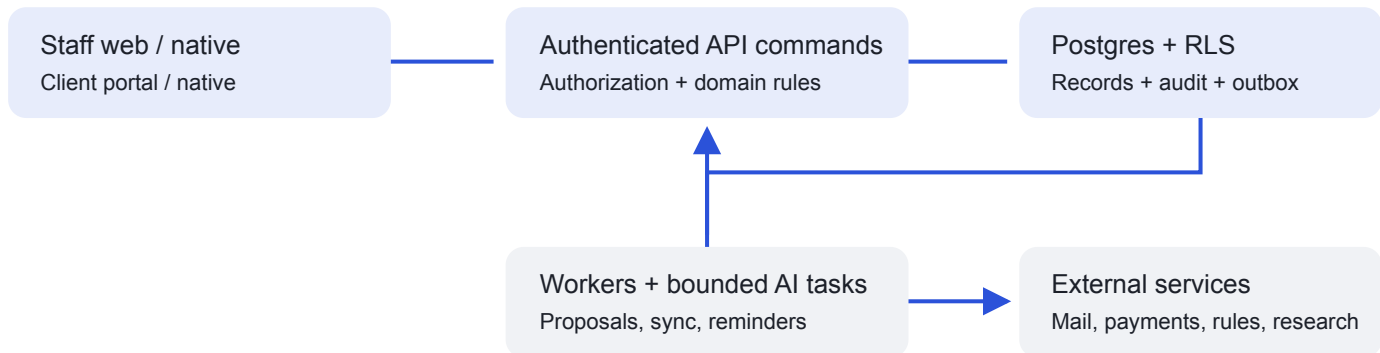

Authorized reads: RLS or API. All writes: bounded server commands. Uploads: API-issued storage URLs.

Rules that remain invariant

- Clients never carry a service-role key or write business tables directly.
- All monetary calculations and cross-entity state changes execute on the server.
- Outbox events commit with business records; jobs can be retried safely.
- Document availability, sharing, and access are authoritative records.
- AI proposals use the same authorized command path as human actions.

Responsibilities

- **Postgres**: durable business state, workflow progress, decisions, financial records, and audit.
- **API**: access checks, validation, transactions, and domain commands.
- **Worker**: bounded processing, provider synchronization, delivery, extraction, and AI tasks.
- **Applications**: interaction, review, permitted reads, and protected draft state.
- **Adapters**: external identity and status mapping with recoverable synchronization.

Provider independence

Use adapters for models, signatures, payments, maintained rules, and research. Provisioning and contract feasibility are prerequisites. Do not substitute silently when an integration is unavailable. Voice architecture remains a separate M22 decision. [S12-S14, S18]

IMPLEMENTATION BLUEPRINT

Domain contracts for nationwide support

Stable interfaces shared by all applications

CONTRACT FAMILY	REQUIRED CONTENT
Identity and access	Active firm, staff capabilities, matter grants, client record grants, publication boundaries.
Practice and matter	Configurable profile/type, multiple parties, optional court, multiple jurisdiction and governing-law references.
Work and workflow	Tasks, prerequisites, owner/backup, trigger facts, template versions, decisions, execution history.
Evidence and documents	Document versions, extraction status, source locations, sharing, template inputs, signature outcomes.
AI proposal	Task version, sources, proposed actions, affected record revisions, review state, execution outcomes.
Financial records	Fee arrangement, actual/confirmed duration, integer cents, invoice history, postings, allocations, independent reconciliation.
Integration	Connection owner, scopes, external object IDs, cursor, provider events, retries, delivery/sync state.
Client publication	Approved status, next step, requests, messages, shared documents, authorized payment references.
Usage and commercial	Deduplicated usage, processing attribution, allowances, caps, explicit overage permission.

Compatibility changes

Move authoritative domain schemas into shared TypeScript/Zod contracts; generate the API client from OpenAPI. Replace display strings and fixture-only flags with structured records. Preserve source IDs during migration and introduce business domains through reversible, versioned migrations.

Record freshness

An approved suggestion must still be checked against current permissions and current affected records when executed. Source existence alone does not prove a legal conclusion or the validity of a deadline.

IMPLEMENTATION BLUEPRINT

Build sequence and dependency map

Work follows domain dependencies rather than independent screen lists

WAVE	MODULES	RESULT
Foundation	M00-M02	Deployable platform, identity/access, universal matter model.
Practice operations	M03-M08	Connected tools, documents, communications, obligations, intake, workflows.
Financial operations	M09-M11	Durable capture, reviewed billing, payments, trust and reconciliation.
Intelligence	M12-M14	Governed retrieval/proposals, seven flagships, document work and research.
Product completion	M15-M20	Staff parity, client apps, reports, practice packs, migration and usage controls.
Core release	M21	Validated national core with staged activation and recovery.
Final module	M22	Receptionist evaluation, architecture decision, implementation and rollout.

Integration points

- M15 staff interfaces develop with each domain; they are not postponed until the backend is finished.
- M18 profile design starts with M02 and M08. Generic nationwide support is a core-launch gate; deep specialties have separate coverage gates.
- M03 provides adapter infrastructure early; financial and other domain sync activates when its records are available.
- M12 cannot bypass M01 permissions, M08 workflow gates, or M10-M11 financial rules.
- M13 client-request/update services feed M16. Published views and access grants are authoritative before exposing client UI.
- M22 uses stable intake, booking, client publication, workflow and usage services after core release.

No delivery-date assumption

Use module milestones and acceptance gates. Estimates require actual team capacity, integration access, and implementation discovery; this blueprint does not invent calendar dates.

MODULE SPECIFICATION

M00 / Engineering platform and delivery foundation

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON None

Make each subsequent feature deployable, observable, and safe to retry. Establish the common execution path before replacing demo behavior.

Implementation steps

1. Audit implemented, demo-only, and missing behavior; convert the agreed module boundaries into a tracked implementation backlog.
2. Configure local, staging, and production environments with isolated credentials and reproducible database migrations.
3. Implement authenticated command context, transaction helpers, request identifiers, consistent errors, and idempotency records.
4. Persist outbox events with business changes; enqueue bounded jobs after commit and record retries, outcomes, and failed work.
5. Add CI for types, lint, relevant tests, builds, migration application, and tenant-isolation checks.
6. Implement structured monitoring, job dashboards, backup routines, restoration rehearsal, and operational runbooks.

Data and contract additions

- Command context: actor, firm, permissions, request ID, idempotency key.
- Durable outbox and job execution records; append-only business audit records.
- Environment configuration and deployment metadata; secrets remain server-side.

API / execution surfaces

- Health/readiness and bounded domain-command conventions.
- Outbox dispatch, retry, and operational inspection interfaces.

Application touchpoints

API, worker, database, deployment infrastructure, and CI.

Acceptance and failure scenarios

- Retry the same command after a network timeout without duplicating its effects.
- Crash after database commit but before queue dispatch; recover the outbox event.
- Restore a backup into staging and reconcile representative records.

Module completion gate

A feature can be deployed, traced from request through job completion, and recovered after interruption.

MODULE SPECIFICATION

M01 / Identity, firm provisioning, and access

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M00

Give staff and clients the correct access to the correct firm and matter. Authentication alone must never imply access to all firm data.

Implementation steps

1. Complete account creation, firm provisioning, invitations, membership changes, and active-firm selection.
2. Define and enforce owner, admin, attorney, paralegal, billing, and readonly capabilities on the server.
3. Implement matter access grants, ethical walls, and role-aware financial permissions.
4. Model clients separately from staff memberships; grant access to specifically published records and client actions.
5. Complete MFA policy, session renewal, device/session controls, and account recovery.
6. Make revocation effective for database reads, files, background work, search, AI retrieval, and local application caches.

Data and contract additions

- Staff membership, active context, role capabilities, matter grants.
- Client identity, client-matter grant, record sharing, session/device records.
- Access-policy revisions and audit entries for invitations, changes, and revocation.

API / execution surfaces

- Provision firm; invite/accept; select context; grant/revoke access.
- Authenticated client access and policy-check interfaces.

Application touchpoints

All staff and client applications; storage, retrieval, and worker authorization.

Acceptance and failure scenarios

- Cross-firm and restricted-matter requests fail, including file and generated-content access.
- A client representative sees only the granted records.
- Revocation invalidates a previously prepared AI action and future downloads.

Module completion gate

Staff and clients can authenticate and complete only the actions authorized for their active context.

MODULE SPECIFICATION

M02 / Contacts, parties, matters, and configurable profiles

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M01

Represent any US legal practice without requiring a court, a single client, or one of the six practice areas currently present in demo types.

Implementation steps

1. Replace the closed frontend practice-area list with configurable practice profiles and extensible matter types.
2. Model people, organizations, aliases, related entities, and prospective/current/former relationships.
3. Add matter-party roles, multiple clients, representatives, responsible lawyers, teams, and assignment history.
4. Separate firm location, lawyer admissions, governing law, venue, agency, and procedural ruleset references.
5. Implement matter creation, configurable fields, notes, activity history, lifecycle state, and search.
6. Support transactions, advisory engagements, agency work, recurring matters, and proceedings without forced litigation fields.

Data and contract additions

- PracticeProfile, MatterType, Contact, PartyRelationship, MatterParty.
- Multiple jurisdiction/venue references; optional court and docket fields.
- Configurable typed fields, assignment history, lifecycle and activity records.

API / execution surfaces

- Matter/contact commands and authorized search/read models.
- Profile and configurable-field administration; related-party lookup.

Application touchpoints

Matters, Contacts, matter detail, search, client selection, and profile settings.

Acceptance and failure scenarios

- Create transactional and advisory matters with no court or hearing.
- Represent one client in several matters and several clients in one matter.
- Add a new practice area and field set without deploying application code.

Module completion gate

Every practice family can use the same authoritative matter and party model with appropriate optional fields.

MODULE SPECIFICATION

M03 / Integration and synchronization framework

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M00, M01, M02

Connect the existing tools firms rely on while making synchronization state, ownership, and failure visible.

Implementation steps

1. Implement connection ownership, OAuth flows, encrypted tokens, authorized scopes, and revocation.
2. Create adapter contracts for external IDs, domain events, pagination, cursors, retries, and reconciliation.
3. Connect Microsoft 365 and Google email/calendar accounts with explicit filing and sharing boundaries.
4. Verify webhooks, reject replays, renew subscriptions, and recover missed notifications with incremental synchronization.
5. Add connection-health views, last successful sync, reconnect actions, and bounded backfill tools.
6. Activate accounting, payment, signature, and other adapters as the corresponding domain modules become available.

Data and contract additions

- Connection, ExternalObjectMap, SyncCursor, WebhookReceipt, SyncRun.
- Private source ownership and explicit matter-filing references.
- Encrypted credentials with access limited to trusted server processes.

API / execution surfaces

- Connect/disconnect; sync status; backfill/retry; verified webhooks.
- Provider adapter contracts and normalized event ingress.

Application touchpoints

Integrations settings, inbox/email filing, calendar, API, and worker. See S15-S17.

Acceptance and failure scenarios

- Expire a subscription, miss a notification, then recover every affected item.
- Replay webhooks without duplicated events.
- Ensure an unfiled private email is not exposed to the wider firm.

Module completion gate

Connected accounts recover from interruption and expose actionable sync status.

MODULE SPECIFICATION

M04 / Documents, templates, storage, and signatures

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M01, M02, M03

Store and share documents durably with version history, source provenance, and controlled execution workflows.

Implementation steps

1. Implement metadata, API-issued upload URLs, upload completion checks, malware scanning, and authorized downloads.
2. Add folders, tags, document versions, replacement history, and matter-linked search.
3. Extract text and preserve page/location references for downstream retrieval and review.
4. Build approved template storage and deterministic field assembly with generated-document provenance.
5. Integrate e-signature envelopes, signer order, status events, completion evidence, and retry-safe callbacks.
6. Support document-specific execution instructions, including workflows that require signing outside the electronic-signature flow.

Data and contract additions

- Document, DocumentVersion, FileObject, ExtractedText, DocumentTemplate.
- Generated artifact inputs, template version, and signature envelope/evidence.
- Sharing grants, extraction status, scan state, and failure records.

API / execution surfaces

- Issue/complete upload; create version; share/revoke; generate document.
- Create/cancel signature envelope and receive signed provider events.

Application touchpoints

Documents, matter detail, uploads, template library, signatures, and worker.

Acceptance and failure scenarios

- Interrupted uploads and failed scans cannot become available documents.
- A shared version remains traceable after a later replacement.
- Signature callbacks update the correct envelope exactly once.

Module completion gate

Every available document is durable, access-controlled, versioned, and linked to its originating matter.

MODULE SPECIFICATION

M05 / Communications, inbox, and notifications

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M03, M04

Create a reliable record of correspondence and requests, with delivery outcomes that users can trust.

Implementation steps

1. Unify filed email, secure client messages, SMS, attachments, and internal communication activity.
2. Maintain conversation ownership, matter links, recipients, consent/preferences, and private-versus-filed boundaries.
3. Implement drafts, approval where required, queued sending, delivered/failed states, and retry-safe delivery.
4. Build inbox views for leads, client requests, approvals, and delivery exceptions.
5. Add templates, notification preferences, quiet hours, reminders, and escalation.
6. Provide deeper Outlook filing and matter context, then extend drafting through the AI modules.

Data and contract additions

- Conversation, Message, Recipient, AttachmentLink, DeliveryAttempt.
- NotificationPreference, ApprovedMessageTemplate, EscalationRecord.
- Separate staff/internal content from published client correspondence.

API / execution surfaces

- Draft/approve/send; file correspondence; acknowledge/read; retry delivery.
- Provider status webhooks and notification routing.

Application touchpoints

Inbox, matter activity, client messages, Outlook support, SMS, email, and push.

Acceptance and failure scenarios

- Failed messages remain visibly failed rather than appearing sent.
- Retries do not deliver the same reminder twice.
- Attachments and conversation history respect individual recipient access.

Module completion gate

Users can determine what was communicated, to whom, when, and with what result.

MODULE SPECIFICATION

M06 / Tasks, calendars, deadlines, and obligations

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M03, M04, M05

Connect dates to preparation, ownership, dependencies, and completion, across court and non-court work.

Implementation steps

1. Implement tasks, owners, backups, prerequisites, reminders, completion evidence, and explicit overrides.
2. Separate events, operational due dates, procedural deadlines, contractual obligations, and externally stated dates.
3. Add a maintained rules-provider adapter and a supported-venue/ruleset coverage registry.
4. Persist triggering facts, service method, timezone, source document, ruleset version, and reviewer decisions.
5. Compare revised orders and changed triggers with existing obligations; present proposed changes for review.
6. Implement conflicts, rescheduling, synchronization recovery, and completion/escalation reporting.

Data and contract additions

- WorkItem, Dependency, CalendarEvent, Obligation, DeadlineCalculation.
- Jurisdiction/ruleset references, trigger facts, calculation/source provenance.
- Reminder schedules, ownership, reviewer history, and override reasons.

API / execution surfaces

- Create/assign/complete work; calculate/propose/review deadlines.
- Calendar sync and changed-trigger impact preview.

Application touchpoints

Tasks, Calendar, Today, matter obligations, docket review, and rules integrations. See S11-S12.

Acceptance and failure scenarios

- A changed order does not silently replace reviewed dates.
- Timezone and daylight-saving transitions preserve intended dates/times.
- Unsupported procedural calculations are explicit; manual sourced dates remain usable.

Module completion gate

Every consequential date has a source, responsible person, follow-through, and review history.

MODULE SPECIFICATION

M07 / Intake, conflicts, engagement, and onboarding

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M04, M05, M06

Move an inquiry into a documented engagement or decline without losing parties, obligations, or follow-up.

Implementation steps

1. Implement lead records, referral sources, configurable forms, consultation booking, and inquiry tracking.
2. Collect the information needed for initial routing and conflict review before broad matter intake.
3. Search prospective, current, former, and related parties; preserve queries, matches, and reviewer decisions.
4. Record attorney clearance, consultation outcomes, scope, fee proposals, engagement, and decline decisions.
5. Generate engagement/non-engagement documents and complete signatures and onboarding requests.
6. Preserve prospective-party records, follow-up, and outstanding obligations when an inquiry is declined.

Data and contract additions

- Lead, IntakeSubmission, Consultation, ConflictCheck, ReviewDecision.
- Engagement scope, fee proposal, signature references, onboarding requests.
- Prospective-party relationships and decline history.

API / execution surfaces

- Submit intake; book consult; run/log conflict check; clear/escalate.
- Prepare engagement/decline; convert to matter with linked history.

Application touchpoints

Public intake, staff Inbox, consultation calendar, engagement, and client onboarding.

Acceptance and failure scenarios

- A fuzzy name match is never automatically treated as clearance.
- A decline preserves relevant records rather than deleting the inquiry.
- Repeated engagement callbacks create only one matter/workflow.

Module completion gate

Inquiry, consultation, review, engagement or decline, and onboarding form one traceable sequence.

MODULE SPECIFICATION

M08 / Editable templates and durable workflow engine

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02-M07

Let firms adapt their operational processes while preserving active matter history and predictable automation.

Implementation steps

1. Define structured stages, approved triggers/actions, prerequisites, simple conditions, role assignments, and review gates.
2. Build draft/test/publish flows and reusable field/document/reminder configuration.
3. Instantiate durable workflow runs with tasks, dependencies, decisions, and execution history.
4. Pin active matters to a published template version; allow controlled instance-level changes.
5. Preview upgrades, rescheduling, reassignment, cancellation, and retroactive changes before application.
6. Deduplicate events, recover failed steps, and expose pending approvals and exceptions.

Data and contract additions

- PlaybookVersion, WorkflowRun, WorkflowStep, Trigger, ApprovedAction.
- Dependency and decision records; source events and execution outcomes.
- Template test cases, version diffs, and matter upgrade plans.

API / execution surfaces

- Draft/test/publish template; instantiate; execute/retry step.
- Approve transition; preview/apply upgrade; cancel or override with history.

Application touchpoints

Playbooks settings, matter progress, work queues, approval views, and worker.

Acceptance and failure scenarios

- Publishing a template does not silently modify active matters.
- Repeated events do not duplicate tasks or messages.
- A failed downstream action remains recoverable without repeating completed actions.

Module completion gate

Users can explain why a step exists, who owns it, what blocks it, and what happened when it ran.

MODULE SPECIFICATION

M09 / Time, expenses, and staff capture

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M04, M05, M06

Make capture durable at the moment work happens, with measured or confirmed time and recoverable offline behavior.

Implementation steps

1. Persist timer start/pause/resume/stop with wall-clock state and crash recovery.
2. Implement manual time, expenses, receipt attachments, notes, and audio capture.
3. Apply effective rates and configured rounding policies while preserving actual duration and original values.
4. Separate billable, no-charge, nonbillable, flat-fee tracking, and written-down entries.
5. Implement protected offline drafts and idempotent sync with access and conflict revalidation.
6. Attach transcription, receipt extraction, narrative suggestions, and day review through M12-M13.

Data and contract additions

- TimerSession, TimeEntry, Expense, ReceiptLink, CaptureDraft.
- Actual/confirmed duration, rate references, rounding policy, revisions.
- Source activity links, audio references, sync state, and conflict records.

API / execution surfaces

- Capture/save; start/pause/stop timer; submit draft; revise entry.
- Link activity and submit suggestion for review without automatic billing.

Application touchpoints

Capture, Time & expenses, timers, mobile offline, receipt and audio workflows.

Acceptance and failure scenarios

- App termination and reconnection do not lose or duplicate captured work.
- Overlapping evidence is not counted twice.
- A calendar duration or email activity alone does not establish actual time worked.

Module completion gate

Capture survives interruption and produces an auditable, accurate billing input.

MODULE SPECIFICATION

M10 / Billing, invoicing, and revenue management

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M04, M05, M07, M09

Turn reviewed work into accurate invoices, receivables, and appropriate collection activity across fee models.

Implementation steps

1. Model hourly, flat/milestone, contingency, mixed, recurring, and split-billing arrangements.
2. Implement pre-bill review, write-downs, approval routing, invoice generation, issuance, and corrections.
3. Preserve issued financial history; use documented adjustments rather than silently rewriting prior outcomes.
4. Represent installment schedules against existing receivables without creating duplicate debt.
5. Add receivable aging, appropriate collection follow-up, retainer requests, and invoice delivery.
6. Implement UTBMS/task coding, LEDES export, and QuickBooks Online synchronization with reconciliation.

Data and contract additions

- FeeArrangement, Prebill, Invoice, InvoiceLine, Adjustment, Receivable.
- InstallmentSchedule, Allocation, billing approval and issuance history.
- Coding profiles, accounting mappings, and synchronization outcomes.

API / execution surfaces

- Review/approve prebill; generate/issue/correct invoice; set schedule.
- Export LEDES; sync financial records; calculate authoritative aggregates.

Application touchpoints

Pre-bill, Invoices, collection views, invoice PDF/export, and accounting integration.

Acceptance and failure scenarios

- Repeated generation cannot invoice one entry twice.
- Installments reconcile to the original outstanding balance.
- Split allocations, adjustments, and accounting exports preserve exact totals.

Module completion gate

Every billed amount is traceable to its fee arrangement, reviewed inputs, and financial history.

MODULE SPECIFICATION

M11 / Payments, trust accounting, and reconciliation

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M03, M05, M06, M10

Maintain trustworthy client and firm financial records with independent reconciliation and controlled money movement.

Implementation steps

1. Integrate payment initiation and provider events for pending, settled, failed, refunded, and disputed outcomes.
2. Separate operating/trust accounts, client allocations, deposits, disbursements, and approved transfers.
3. Use balanced traceable postings; record corrections and reversals without losing prior evidence.
4. Import independent bank evidence and compare it with book and client-ledger balances.
5. Implement discrepancy review, reconciliation sign-off, locked reports, and audit exports.
6. Apply jurisdiction-specific notice, review, retention, and account policies through sourced configuration.

Data and contract additions

- Account, Posting, Payment, Allocation, TransferApproval, Reversal.
- BankEvidence, Reconciliation, Discrepancy, SignedReport.
- Jurisdiction-policy references and change/review history.

API / execution surfaces

- Initiate/allocate payment; approve transfer; record/reverse posting.
- Import statement; reconcile; resolve discrepancy; sign/export report.

Application touchpoints

Payments, Trust, client balances, audit reports, and provider/accounting integrations. See S13.

Acceptance and failure scenarios

- Provider replay cannot allocate funds twice.
- One client balance cannot fund another client matter improperly.
- Reconciliation detects a real mismatch rather than deriving every balance from one source.

Module completion gate

Financial states reconcile with independent evidence and every movement has authority and provenance.

MODULE SPECIFICATION

M12 / AI platform, retrieval, and proposal governance

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M01, M02, M04, M05, M08

Provide a reusable AI layer that respects source permissions, records evidence, and proposes bounded actions.

Implementation steps

1. Implement provider adapters, processing policy, usage attribution, and configurable task/model routing.
2. Extract and index source content with firm, matter, version, visibility, and deletion metadata.
3. Filter retrieval by current access before constructing task context; separate untrusted content from tool authority.
4. Produce structured outputs and source-linked proposals instead of unrestricted database or provider writes.
5. Revalidate permissions and affected record versions before execution; reject or regenerate stale proposals.
6. Build an evaluation corpus and track corrections, unsupported claims, latency, failures, and processing costs.

Data and contract additions

- SourceReference, ExtractedChunk, RetrievalContext, AIJob, AIProposal.
- ProposedAction, affected record versions, reviewer decision, evaluation result.
- Policy, retention, model/task version, and usage metadata.

API / execution surfaces

- Run bounded AI task; inspect proposal/source; approve/reject/regenerate.
- Authorized retrieval and action execution through normal domain commands.

Application touchpoints

Shared AI services, worker processing, source viewers, review UI, and evaluation tools. See S10.

Acceptance and failure scenarios

- Restricted and deleted sources do not appear in answers or cached outputs.
- Instructions inside a document cannot authorize an external action.
- Stale proposals cannot overwrite newer facts or revoked access.

Module completion gate

AI output remains inspectable and cannot bypass application controls.

MODULE SPECIFICATION

M13 / Seven flagship connected automations

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M06, M08-M12

Deliver the product promise through end-to-end follow-through rather than isolated suggestion buttons.

Implementation steps

1. Implement incoming information to matter updates, tasks, dates, and follow-up proposals.
2. Expose next meaningful steps, dependencies, stalled work, and preparation gaps with explanations.
3. Track requested documents, missing items, completeness review, and approved follow-up.
4. Prepare client updates from verified activity; connect staff dictation to notes, tasks, dates, and time drafts.
5. Connect actual or confirmed work to day review, pre-bill preparation, invoice approvals, and collections.
6. Generate preparation/handoff briefs; group related proposals and show execution outcomes.

Data and contract additions

- Flagship workflow instances built on M08 and M12 contracts.
- Request/completeness state, blockers, grouped proposals, brief source sets.
- Feedback and outcome measures for review effort and workflow completion.

API / execution surfaces

- Start/inspect flagship workflow; review related changes; execute permitted steps.
- Publish approved client update; produce brief; inspect pending/failed follow-through.

Application touchpoints

Today, Inbox, matter progress, day review, client requests/updates, brief and approval screens.

Acceptance and failure scenarios

- Each flagship runs from source event through durable outcomes.
- An upload alone does not mark legal/document completeness.
- Users can recover partial execution without duplicating completed work.

Module completion gate

All seven capabilities work with real services and persist across navigation, sessions, and retries.

MODULE SPECIFICATION

M14 / Document intelligence and external legal research

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M04, M08, M12

Support substantive document work using matter evidence, approved templates, and licensed research sources.

Implementation steps

1. Generate drafts from approved templates and matter facts with traceable inputs and versions.
2. Compare document versions and related documents, identifying cited discrepancies.
3. Review against firm-defined criteria and distinguish evidence from proposed interpretation.
4. Build factual chronologies with source passages, date uncertainty, and unresolved contradictions.
5. Integrate specialist external research through a licensed adapter, retaining authoritative source links.
6. Add DOCX export, Word assistance, review/accept/reject flows, and reviewed artifact history.

Data and contract additions

- DraftArtifact, ReviewFinding, Comparison, ChronologyEvent, ResearchRequest.
- Source/version links, uncertainty, edits, reviewer decisions, final artifact.
- Partner entitlement and research-result provenance.

API / execution surfaces

- Draft/review/compare; generate chronology; accept edits; export DOCX.
- Run licensed research; open source authority; retain reviewed version.

Application touchpoints

Document workspace, template library, Word integration, and partner research. See S14, S21.

Acceptance and failure scenarios

- Findings point to the correct document version and location.
- Contradictory evidence remains visible rather than being silently resolved.
- Legal work product is reviewed before consequential external use.

Module completion gate

Users can inspect, correct, and retain the sources and reasoning inputs behind generated work.

MODULE SPECIFICATION

M15 / Production staff web and native experience

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON Incremental alongside M01-M14

Connect the existing design investment to durable behavior on web, iOS, and Android.

Implementation steps

1. Replace fixture hooks with shared production contracts feature by feature.
2. Split the native preview state machine into maintainable routes, forms, and feature slices.
3. Complete Today, Inbox, Matters, Contacts, Capture, Calendar, Documents, Time, Billing, Trust, Reports, and Settings.
4. Implement production deep links, push, session recovery, protected local drafts, and offline synchronization.
5. Retain the Clepso design system and implement loading, empty, error, accessibility, and reduced-motion states.
6. Exercise platform parity for the seven flagships and every launch-critical financial/client interaction.

Data and contract additions

- Shared view contracts from domain modules; no duplicated business rules.
- Native draft/sync metadata and current authorization context.
- Ephemeral UI state separated from authoritative server state.

API / execution surfaces

- Existing feature hooks map to authorized reads and API commands.
- Deep links resolve to accessible records with explicit unavailable states.

Application touchpoints

Staff web and Expo applications; responsive shell, routes, capture, and domain screens.

Acceptance and failure scenarios

- Complete required journeys on web, iOS, and Android using real data.
- Offline work retries safely and revoked access clears protected caches.
- Application restart preserves valid drafts and timer state.

Module completion gate

Staff can complete launch-critical work across platforms without relying on preview behavior.

MODULE SPECIFICATION

M16 / Client portal and native client applications

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M01, M04-M06, M08, M10-M13

Give clients a useful place to understand progress, complete requests, communicate, sign, and pay.

Implementation steps

1. Build the web portal and shared Clepso native apps with firm branding after authentication.
2. Implement invitations, identity verification, case selection, and individual client/representative grants.
3. Display published progress, next steps, requested actions, and approved attorney updates.
4. Implement secure conversations, camera/file uploads, signature requests, invoices, plans, and receipts.
5. Show request receipt separately from staff review/completeness and subsequent progress.
6. Add accessible onboarding, push preferences, session recovery, and consistent information across platforms.

Data and contract additions

- ClientMatterGrant, PublishedMatterUpdate, ClientActionRequest.
- Shared document/signature/payment references and conversation access.
- Client notification preferences and access/publication revisions.

API / execution surfaces

- Read published case view; reply; fulfill request; sign; initiate payment.
- Staff publish/revoke/update client-visible information through approved commands.

Application touchpoints

Client web portal, shared iOS/Android apps, and staff publishing/request management.

Acceptance and failure scenarios

- Internal activity and unpublished proposals are never visible to clients.
- One representative grant does not expose every client record.
- Web/iOS/Android show consistent progress, requests, balances, and delivery outcomes.

Module completion gate

Clients can complete the intended actions and understand what happens next.

MODULE SPECIFICATION

M17 / Reports, workload, and firm management

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M06, M08-M13

Help the firm identify operational and financial issues with metrics that reconcile to underlying records.

Implementation steps

1. Define authoritative utilization, realization, collection, aging, and profitability calculations.
2. Build workload, ownership, backup coverage, stalled-work, and preparation views.
3. Add matter budgets, fee-model views, and actual-versus-estimated cost/progress reporting.
4. Provide filters, custom reports, scheduled delivery, and exports.
5. Enforce matter and financial access in every aggregate, drill-down, and generated report.
6. Label incomplete imported data and retain calculation definitions and reporting timestamps.

Data and contract additions

- ReportDefinition, MetricDefinition, Budget, ReportRun, Schedule.
- Source period, inclusion rules, permission scope, and completeness metadata.
- Drill-down references and delivery outcomes.

API / execution surfaces

- Run/filter/export report; inspect metric inputs; schedule delivery.
- Authorized workload and financial aggregate read models.

Application touchpoints

Reports, Today firm view, workload, budgets, and scheduled exports.

Acceptance and failure scenarios

- Reports reconcile with source records and payment/ledger totals.
- Restricted matters are not leaked by counts or drill-downs.
- Scheduled reports use current access and approved destinations.

Module completion gate

Firm managers can inspect both a metric and the records explaining it.

MODULE SPECIFICATION

M18 / Nationwide profiles and specialty modules

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M04, M06-M14

Support every practice family through a universal core and clearly labeled specialty capabilities.

Implementation steps

1. Publish an extensible catalog and operational starter profiles across all practice families.
2. Package field definitions, party roles, document requirements, stages, fee structures, and review instructions.
3. Separate generic operational templates from jurisdiction-validated procedural rules and legal requirements.
4. Add specialist forms, calculations, portfolio tracking, records workflows, and partner integrations in documented waves.
5. Maintain a coverage matrix for jurisdiction, venue, module version, evidence, and validation status.
6. Test each released pack with representative matters and allow firm customization without changing application code.

Data and contract additions

- PracticePackVersion, FieldProfile, WorkflowProfile, DocumentRequirement.
- Specialist capability descriptors, integration entitlements, and coverage records.
- Sourced jurisdiction/venue references, review status, and pack change history.

API / execution surfaces

- Install/configure/publish pack; inspect coverage; preview upgrade.
- Extend profiles and invoke released specialist capabilities through bounded interfaces.

Application touchpoints

Practice catalog, firm setup, matter creation, template library, and specialty workspaces.

Acceptance and failure scenarios

- Every listed family can operate in core matter management at launch.
- Transactional and agency packs do not require litigation-only fields.
- Coverage labels distinguish generic support from validated specialist automation.

Module completion gate

All areas have core support; released specialist claims match tested functionality.

MODULE SPECIFICATION

M19 / Migration, export, closure, and retention

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M02, M04, M07, M10, M11

Make switching, closing files, and leaving the product operationally credible.

Implementation steps

1. Build staged import pipelines for supported competitor exports and spreadsheets.
2. Map identifiers, parties, matters, relationships, documents, access restrictions, and financial history.
3. Validate counts and balances; produce source-to-target reconciliation and exception reports.
4. Require explicit acceptance of migration results before activating operational records.
5. Implement file closure, final accounting, return/export, archives, legal holds, and configurable retention.
6. Provide complete account-exit exports with readable financial, document, and relationship records.

Data and contract additions

- ImportBatch, SourceMap, ImportException, ReconciliationReport.
- ClosureChecklist, Archive, LegalHold, RetentionPolicy, ExportRun.
- Accepted opening financial positions and preservation of historical references.

API / execution surfaces

- Dry-run/import/reconcile/accept; close/archive; hold; export.
- Controlled retention review and exception resolution.

Application touchpoints

Migration onboarding, administrator tools, closure, archives, and export worker.

Acceptance and failure scenarios

- Counts, relationships, receivables, and trust balances reconcile.
- Importing documents does not publish them to clients automatically.
- Legal holds prevent destructive retention actions.

Module completion gate

Migration and export results can be checked independently and accepted by the firm.

MODULE SPECIFICATION

M20 / Subscriptions, AI usage, and spending controls

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M01, M03, M10-M14

Provide predictable commercial behavior without obscuring variable service usage.

Implementation steps

1. Implement subscriptions, seats, plan entitlements, renewals, cancellations, and verified subscription events.
2. Record deduplicated usage for AI, messaging, storage, and later voice with clear attribution.
3. Support included allowances, visible meters, configured caps, and explicit overage opt-in.
4. Enforce limits gracefully with resumable or clearly failed work, rather than losing submitted inputs.
5. Reconcile supplier usage and customer-facing charges; expose explainable usage history.
6. Keep essential access/confidentiality controls available independently of premium productivity features.

Data and contract additions

- Subscription, Entitlement, UsageEvent, Allowance, SpendLimit.
- Provider usage references, billing periods, adjustments, and meter projections.
- No invented launch prices or allowances: commercial configuration follows measured costs.

API / execution surfaces

- Change subscription; inspect usage; configure cap/overage; reconcile events.
- Entitlement and quota checks in bounded processing commands.

Application touchpoints

Plan/usage settings, processing limits, billing administration, and commercial monitoring.

Acceptance and failure scenarios

- Provider retries do not charge the same work twice.
- A cap cannot turn a queued action into an apparently completed action.
- Cancellation and plan changes preserve access to authorized export workflows.

Module completion gate

Usage and charges are understandable, bounded, and linked to actual processing.

MODULE SPECIFICATION

M21 / Nationwide validation and core launch

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON M00-M20; released profiles and specialty packs

Release a credible national core product after exercising real journeys, recovery, and cross-platform behavior.

Implementation steps

1. Recruit pilots across firm sizes, practice families, fee models, and jurisdictions.
2. Exercise complete journeys on configured integrations using permissioned or synthetic files.
3. Validate tenant/matter boundaries, migration reconciliation, financial invariants, and backup restoration.
4. Load representative 50-lawyer workloads and verify supported desktop/mobile environments.
5. Compare flagship handling time, correction effort, completion, and confidence with current firm processes.
6. Enable capabilities in stages, monitor failures/corrections/costs, and document launch readiness.

Data and contract additions

- ValidationDataset, PilotFeedback, AcceptanceResult, ReleaseChecklist.
- Coverage matrix, supported environment list, operational runbooks.
- Measured outcomes with baselines; no unverified product-improvement claims.

API / execution surfaces

- Staged feature activation and observable rollback/disable controls.
- Operational inspection, support escalation, incident/recovery workflows.

Application touchpoints

All applications, integrations, operations, pilots, and release delivery.

Acceptance and failure scenarios

- Core workflows succeed without receptionist availability.
- Recovery drills preserve financial and workflow records.
- Every release claim maps to working behavior, coverage evidence, and a tested journey.

Module completion gate

The full core suite can launch nationally with clear supported automation and independent operation.

MODULE SPECIFICATION

M22 / AI receptionist: evaluate, decide, then implement

Implementation sequence, contracts, verification, and completion gate

DEPENDS ON Stable core release; M01, M05-M08, M16, M20

Implement the receptionist last, after comparing viable approaches against the same operational and cost requirements.

Implementation steps

1. Define inbound lead and existing-client journeys, authentication, consent, booking, escalation, and fallback.
2. Compare an application-owned voice agent, n8n-assisted orchestration, managed APIs, and a hybrid architecture.
3. Test representative calls, interruptions, transfer failure, unavailable staff, disconnects, and identity ambiguity.
4. Compare latency, reliability, data handling, variable cost, customization, and maintenance; publish a decision record.
5. After the implementation approach is selected, connect it through bounded Clepso tools and usage controls.
6. Pilot overflow/after-hours calls before broader activation and review results before enabling additional autonomy.

Data and contract additions

- CallSession, ConsentState, CallerVerification, IntakeSummary, ToolAttempt.
- Transfer/booking outcomes, callback requests, transcript policy, usage records.
- Architecture decision remains deferred; no provider is committed here.

API / execution surfaces

- Authenticated, bounded tools for intake, booking, approved status, and routing.
- Session events, provider callbacks, review, fallback, and usage reporting.

Application touchpoints

Telephony service, firm routing/settings, intake review, and receptionist monitoring. See S19-S20.

Acceptance and failure scenarios

- Caller ID alone cannot authorize case disclosure.
- Failed transfers produce a clear fallback with a durable staff request.
- The voice service cannot bypass conflict, legal-review, or payment controls.

Module completion gate
The evaluated solution handles normal and failed journeys without becoming a core-product dependency.

POST-LAUNCH / FINAL MODULE No voice provider or architecture is selected.

IMPLEMENTATION BLUEPRINT

Practice coverage: shared foundation

Every practice family uses the core; specialist depth is explicit

PRACTICE FAMILY	UNIVERSAL CORE + STARTER PROFILE	DEDICATED SPECIALTY CAPABILITIES
Civil litigation / commercial disputes	Parties, evidence, tasks, calendar, discovery requests, fees, communications.	Reviewed deadline chains, discovery/evidence tools, experts, litigation preparation.
Injury / malpractice / insurance defense	Records, contacts, costs, matter progress, client updates, billing models.	Medical/claim workflows, damages/cost records, liens/settlement steps, insurer coding.
Family / juvenile	Parties, representative access, requests, hearings, fees, communication.	Disclosure tracking, evidence organization, client decisions, reviewed court workflows.
Criminal defense	Matter evidence, hearing calendar, scope, tasks, fee arrangements.	Evidence requests, preparation, reviewable procedural obligations, appointment-related billing.
Estates / probate / trusts / elder law	People/entities, assets as configured fields, documents, tasks, progress.	Fiduciary administration, inventories, beneficiaries, accounts, jurisdiction-specific closure.
Immigration / benefits	Agency references, notices, evidence requests, documents, tasks, milestones.	Form/evidence packages, notice workflows, partner integrations, reviewed agency obligations.

Launch interpretation

Core and configurable operational starter profiles support every family. A specialist form, calculation, or integration is advertised only when released and validated. Firms can customize profiles; custom configuration is distinguishable from maintained procedural content.

Reusable pack contents

A pack combines field definitions, party roles, document requests, operational stages, approval gates, fee configuration, client-facing explanations, integration capabilities, and coverage evidence. Packs are versioned and existing matters retain their selected version.

IMPLEMENTATION BLUEPRINT

Practice coverage: extensible specialties

Transactions, portfolios, agencies, and custom practice areas

PRACTICE FAMILY	UNIVERSAL CORE + STARTER PROFILE	DEDICATED SPECIALTY CAPABILITIES
Bankruptcy / debtor-creditor	Clients, financial evidence, documents, agency/court steps, deadlines, fees.	Petition/form packages, trustee requests, hearings, specialized calculations/integrations.
Corporate / commercial / contracts / tax	Entities, agreements, diligence, advisory scope, tasks, obligations, milestones.	Transaction checklists, recurring obligations, renewals, specialist authority/form workflows.
Real estate / landlord-tenant / construction	Property/project fields, parties, documents, requests, tasks, costs.	Closing/escrow-related workflow, notices, project dependencies, reviewed local requirements.
Employment / workers compensation	Claim/agency details, evidence, requests, hearings, fees, costs.	Agency steps, specialized claims, settlements, approval/calculation workflows.
Intellectual property	Portfolio relationships, documents, agreements, obligations, tasks.	Applications, renewals, prosecution, licensing and maintained partner docketing.
Regulatory / administrative / appellate	Forums, submissions, records, obligations, assignments, evidence.	Reviewed forum-specific processes and specialist content/integrations.
Healthcare / education / environmental / other	Configurable matter types, relationships, fields, requests, documents, work and fees.	Dedicated profile packs and integrations added through the same extension model.

Levels of support

LEVEL	MEANING
Core	Matter, people, documents, communications, work, fees and access support.
Starter	Configurable operational profile with appropriately optional fields.
Reviewed pack	Tested specialist workflows with documented jurisdiction applicability.
Integration	Released specialist service with explicit entitlement and coverage.

IMPLEMENTATION BLUEPRINT

Jurisdiction coverage and rule maintenance

Broad app availability with precise automation evidence

Catalog and matter configuration

- Support states, DC, federal forums, agencies, and US territories as configurable jurisdiction records.
- Keep venue, court, governing law, lawyer admissions, and firm address independent.
- Allow several jurisdiction references on one matter, or no court at all.
- Show which specific procedural, financial, document, and specialist behaviors are supported for the selected configuration.

COVERAGE RECORD	WHAT MUST BE RETAINED
Rule / policy source	Provider or primary source, link/reference, applicability, effective/version information.
Calculation inputs	Trigger fact, service method where relevant, timezone, venue, selected ruleset.
Review evidence	Reviewer, accepted output, date, corrections, override reason, validation history.
Change management	Provider update, affected matters, difference preview, review and execution outcome.
Unsupported behavior	Explicit unavailable calculation; sourced manual entry remains possible.
Pack status	Generic operational support versus reviewed jurisdiction-specific functionality.

Trust and billing configuration

Implement common accounting controls centrally, while keeping jurisdiction-specific notices, approvals, retention, and execution requirements in reviewed configuration. Do not extrapolate a California example into a nationwide default.

Scope of coverage

A provider offering courts in all states does not establish identical coverage for every court, agency, judge order, practice, or filing channel. Match actual released capabilities to the selected matter context. [S11-S12]

IMPLEMENTATION BLUEPRINT

Flagship journeys: information becomes work

Three concrete demonstrations of connected follow-through

1. Revised order to reviewed work

1. Receive and file an order; identify the likely matter or request clarification.
2. Extract stated facts and dates with document locations; compare against current obligations.
3. Prepare related task/date changes and a client-update draft with source/version references.
4. The responsible reviewer accepts or corrects the coherent proposal set.
5. Execute permitted changes; synchronize calendars and assignments; expose failed follow-through.
6. Preparation views and client publication use the reviewed state, not the unapproved extraction.

2. Document request to complete next step

1. Send a structured request for identified documents through an approved channel.
2. The client uploads against each item and sees receipt status.
3. Extraction flags missing periods, unreadable files, or inconsistent information.
4. Staff review completeness; the request remains open until its requirements are satisfied.
5. Permitted reminders and escalation follow template configuration.
6. Workflow progress and the published next step reflect confirmed completion.

3. Voice memo to coordinated follow-through

A lawyer dictates after a hearing. Clepso preserves the audio/note, proposes the matter update and tasks, identifies dates needing review, and prepares a confirmed-duration time draft. Related changes are reviewed together. Native offline capture can synchronize later without repeating actions.

IMPLEMENTATION BLUEPRINT

Flagship journeys: progress, money, preparation

Four more required end-to-end experiences

4. Explainable blocker detection

The matter view shows the next meaningful step, responsible person, prerequisites, and unresolved external requests. It distinguishes missing information from overdue action. Staff can resolve a blocker, reassign work, or record an override with an explanation.

5. Verified activity to client update

Clepso assembles a draft from reviewed activity: what changed, what happens next, expected dates where established, what the client must do, and relevant cost information. Staff approve publication. Web and native clients read the same published record.

6. Actual work to accurate billing

1. Link measured or user-confirmed activity to capture review and remove duplicates.
2. Review fee arrangements, narratives, expenses, write-downs, and approval requirements.
3. Issue invoices and track delivery against durable financial records.
4. Receive provider payment outcomes and allocate funds once.
5. Use accurate balances for reminders, plans, retainers, and financial reporting.

7. Preparation and handoff brief

Before a meeting, hearing, reassignment, or coverage handoff, produce a current brief containing relevant facts, recent changes, obligations, missing information, unresolved discrepancies, and source links. Filter every source by the reader's current access.

What makes these flagship capabilities

The product reduces reconstruction and coordination across tools. Evaluate the entire sequence, including correction and recovery, rather than only the speed of generating a summary.

IMPLEMENTATION BLUEPRINT

Acceptance: domain and access correctness

Meaningful scenarios tied to business invariants

AREA	SCENARIOS	PASS CONDITION
Authorization	Cross-firm reads/writes; ethical walls; client representatives; signed files; AI retrieval.	No unauthorized record, attachment, source, or aggregate is disclosed.
Nationwide model	Non-court transactions; agency work; multi-jurisdiction matter; new practice profile.	The model supports each without hard-coded California or litigation assumptions.
Workflows	Repeated event; interrupted step; upgrade; manual override; changed order.	No duplicate effects, lost history, or silent consequential changes.
Documents	Interrupted upload; failed scan; new version; revoked sharing; signature replay.	Only available, authorized, correctly versioned documents are exposed.
Billing	Hourly/flat/mixed; splits; write-downs; installments; repeated generation.	Exact totals and one receivable; reviewed fee inputs remain traceable.
Money	Pending/settled/failed; refunds; disputes; replayed event; client allocation.	Provider and ledger states reconcile without double application.
Reconciliation	Independent bank mismatch; unresolved discrepancy; sign-off; later correction.	Differences are found, resolved, and preserved in auditable reports.
AI	Restricted source; prompt injection; stale proposal; contradiction; missing citation.	Bounded tools and review remain enforced; evidence and uncertainty remain visible.

Tests follow risk and change

Use shared domain/unit tests for calculations and decisions, integration tests for permissions and delivery/recovery, and end-to-end tests for launch journeys. Avoid tests that only restate fixture implementation.

IMPLEMENTATION BLUEPRINT

Acceptance: delivery, recovery, and platforms

Complete user journeys under realistic interruption

AREA	SCENARIOS	PASS CONDITION
Synchronization	Expired tokens/subscriptions, missed events, provider outage, retry/backfill.	Recover source changes and show useful connection health.
Messaging	Wrong recipient prevented, failed delivery, repeated reminder, stale approval.	Delivery states are truthful and messages are not duplicated.
Offline native	App killed, draft saved, access revoked, reconnect, timer resumed.	Valid work survives; unauthorized cached data and actions are revalidated.
Client platforms	Invite, select case, fulfill request, sign, message, view/pay invoice.	Web/iOS/Android show consistent approved information and outcomes.
Migration	Source counts, party links, files, invoice balances, trust positions, restrictions.	Exceptions are explicit and the firm accepts reconciled results.
Operations	Backup restoration, queue failure, database outage, long processing, cap reached.	No silent loss of records or apparently successful uncompleted work.
Scale	Representative 50-lawyer concurrency and realistic document/financial histories.	Key user journeys remain usable; measured limits guide capacity.
Receptionist (later)	Consent refusal, interrupted conversation, unverified client, failed transfer.	Fallback is truthful and durable; case access and action gates hold.

Performance and value measurement

Establish baselines for handling time, review/correction effort, workflow completion, sync lag, processing latency, and actual service costs. Agree performance thresholds after representative data and staffing are available. No benchmark improvement or price is asserted by this document.

Pilot composition

Recruit across solo/small/larger initial firms, hourly/flat/contingency work, court/non-court practice, and multiple jurisdictions. There is currently no established advisory group; recruitment is an implementation task.

IMPLEMENTATION BLUEPRINT

Core launch and operating procedures

Release the core independently of the final receptionist module

Core release checklist

- M00-M20 meet their module gates; every required platform and all seven flagships use production services.
- Universal practice profiles and release-designated specialty capabilities have honest coverage labels.
- Permissions, independent financial reconciliation, migration, backups and recoverability have been exercised.
- Integration access, commercial terms, actual costs and credential provisioning are completed for advertised services.
- Native distribution, email/OAuth configuration, notification delivery and supported environments are verified.
- Support runbooks, exception queues, monitoring and firm-level activation controls are ready.
- Pilot feedback and recorded acceptance results support each release claim.

Staged activation

1. Complete domain modules and realistic acceptance datasets in local/staging environments.
2. Enable bounded features for pilot firms and compare against their current processes.
3. Activate low-risk automation under approved templates; keep consequential review gates.
4. Monitor correction effort, failed delivery/sync, unresolved jobs, ledger discrepancies, and spend.
5. Resolve release-blocking issues and broaden activation with clear coverage communication.
6. Begin M22 evaluation separately after the core operates reliably.

Operational ownership

Assign owners for integration failures, deadline review exceptions, financial discrepancies, client access requests, AI evaluations, and recovery drills. Monitoring must lead to an actionable work queue, not merely collect logs.

IMPLEMENTATION BLUEPRINT

External dependencies and deliberate deferrals

Integration feasibility and the last-module architecture decision

DEPENDENCY	IMPLEMENTATION PREREQUISITE
Microsoft / Google	OAuth scopes, verification where required, administrator permissions, subscription renewal and recovery. [S15-S17, S21]
Maintained court rules	Licensed partner access, supported venue mapping, version/change handling, reviewable calculations. [S11-S12]
Payments / accounting	Operating/trust behavior, provider events, fees/disputes/refunds, QuickBooks reconciliation. [S13]
Signatures	Provider access, signer evidence, document-specific execution instructions, reliable callbacks.
External research	Licensed API/entitlements and sourced results. Vincent is a candidate integration, subject to terms. [S14]
AI models / processing	Documented retention/processing terms, task suitability, evaluations, measured cost and quotas. [S10]
AI receptionist	No supplier selected; compare application-owned, n8n-assisted, managed-API and hybrid approaches in M22. [S19-S20]

Receptionist comparison criteria

Evaluate the same inbound lead and verified-client scenarios across options: latency, interruptions, routing, booking accuracy, unavailable humans, disconnects, data handling, tool permissions, cost per completed call, maintenance, and portability. n8n can coordinate tools and callbacks; a live conversation also needs telephony and real-time audio processing.

Decisions that remain intentionally open

Receptionist architecture and supplier, final commercial pricing/allowances, team-based estimates, and provider contracts. These are explicit work items; they are not hidden assumptions or permission to invent production claims.

IMPLEMENTATION BLUEPRINT

Sources and evidence

Research, repository inspection, and competitor materials

S01 How law firms work — an operating map

Provided research document; September 30, 2026. The exported text was reviewed; embedded figure placeholders remain unavailable.

S02 Repository audit

Local source and documentation, checked October 1, 2026: CLAUDE.md; staff web/native READMEs; API module; worker; tenancy schema; frontend domain types.

S03 Clio Manage AI

Documented practice-management AI capabilities.

<https://help.clio.com/hc/en-us/articles/29657814904475-What-is-Manage-AI-and-How-to-Access-it>

S04 MyCase Case Assistant and Smart Time Finder

Case retrieval and passive time-capture descriptions.

<https://supportcenter.mycase.com/en/articles/12267713-8am-iq-case-assistant>

S05 Smokeball Archie

Matter assistance, drafting, review, source references and integrations.

<https://www.smokeball.com/archie-ai>

S06 Filevine task management

Task/deadline and records-related capabilities.

<https://www.filevine.com/platform/case-management-software/legal-task-management/>

S07 Litify ACE announcement

Agentic workflow and proactive case-management positioning.

<https://www.litify.com/news/litify-launches-litify-ace-the-agentic-case-expert-to-power-proactive-legal-workflows>

S08 Actionstep Intelligence

Operational AI capabilities and roadmap labeling.

<https://www.actionstep.com/artificial-intelligence/>

S09 PracticePanther plans and capabilities

Practice-management, communication and automation baseline.

<https://www.practicepanther.com/pricing/>

S10 ABA Formal Opinion 512

Generative AI competence, confidentiality, supervision, communication and fees.

https://www.americanbar.org/content/dam/aba/administrative/professional_responsibility/ethics-opinions/aba-formal-opinion-512.pdf

S11 CalendarRules court list

Public court/agency coverage evidence; exact enabled coverage requires verification.

<https://www.calendarrules.com/court-list>

Attribution

Vendor materials support capability descriptions, not independent superiority or performance claims. The operating map is a synthesis; this document does not claim to have independently audited every statistic or source it contains.

IMPLEMENTATION BLUEPRINT

Sources and decision history

Implementation references and confirmed changes

- S12 LawToolBox API documentation**
 Partner API and access prerequisites.
<https://api.lawtoolbox.com/api>
- S13 LawPay trust-account protections**
 Provider description of operating/trust account protections.
<https://www.lawpay.com/features/compliance/>
- S14 vLex developer API catalog**
 External legal-research integration feasibility; licensing still required.
<https://developer.vlex.com/apis>
- S15 Microsoft Graph lifecycle notifications**
 Subscription renewal, removed subscriptions and missed-change recovery.
<https://learn.microsoft.com/en-us/graph/change-notifications-lifecycle-events>
- S16 Gmail push notifications**
 Watch/notification lifecycle and synchronization implementation.
<https://developers.google.com/workspace/gmail/api/guides/push>
- S17 Gmail API scopes**
 Authorization scopes and verification implications.
<https://developers.google.com/workspace/gmail/api/auth/scopes>
- S18 BullMQ idempotent jobs**
 Retry-safe background execution conventions.
<https://docs.bullmq.io/patterns/idempotent-jobs>
- S19 n8n license FAQ**
 Customer workflow/credential hosting and embedding commercial terms.
<https://support.n8n.io/article/can-i-use-your-license-for-my-use-case>
- S20 LiveKit agent-assisted transfer**
 Example technical feasibility for one application-owned voice option; not a selected implementation.
<https://docs.livekit.io/telephony/features/transfers/warm/>
- S21 Outlook add-in overview**
 Add-in supported environments and capability differences.
<https://learn.microsoft.com/en-us/office/dev/add-ins/outlook/outlook-add-ins-overview>

Decision history

Nationwide scope replaces California-first product positioning. All practice families receive configurable core support, with dedicated specialties delivered as modules. Initial firm sizes remain approximately 50 lawyers or fewer. Client web and shared native apps, both email/calendar ecosystems, editable templates, all seven flagships, document intelligence, and controlled autonomy remain required. The receptionist moves to the final post-core module and its architecture is explicitly reopened.
